


Hospital Intake Workflow Optimization

Executive Project Update | Simulated Portfolio Case Study

Executive Dashboard

Operational improvement and project controls at closeout

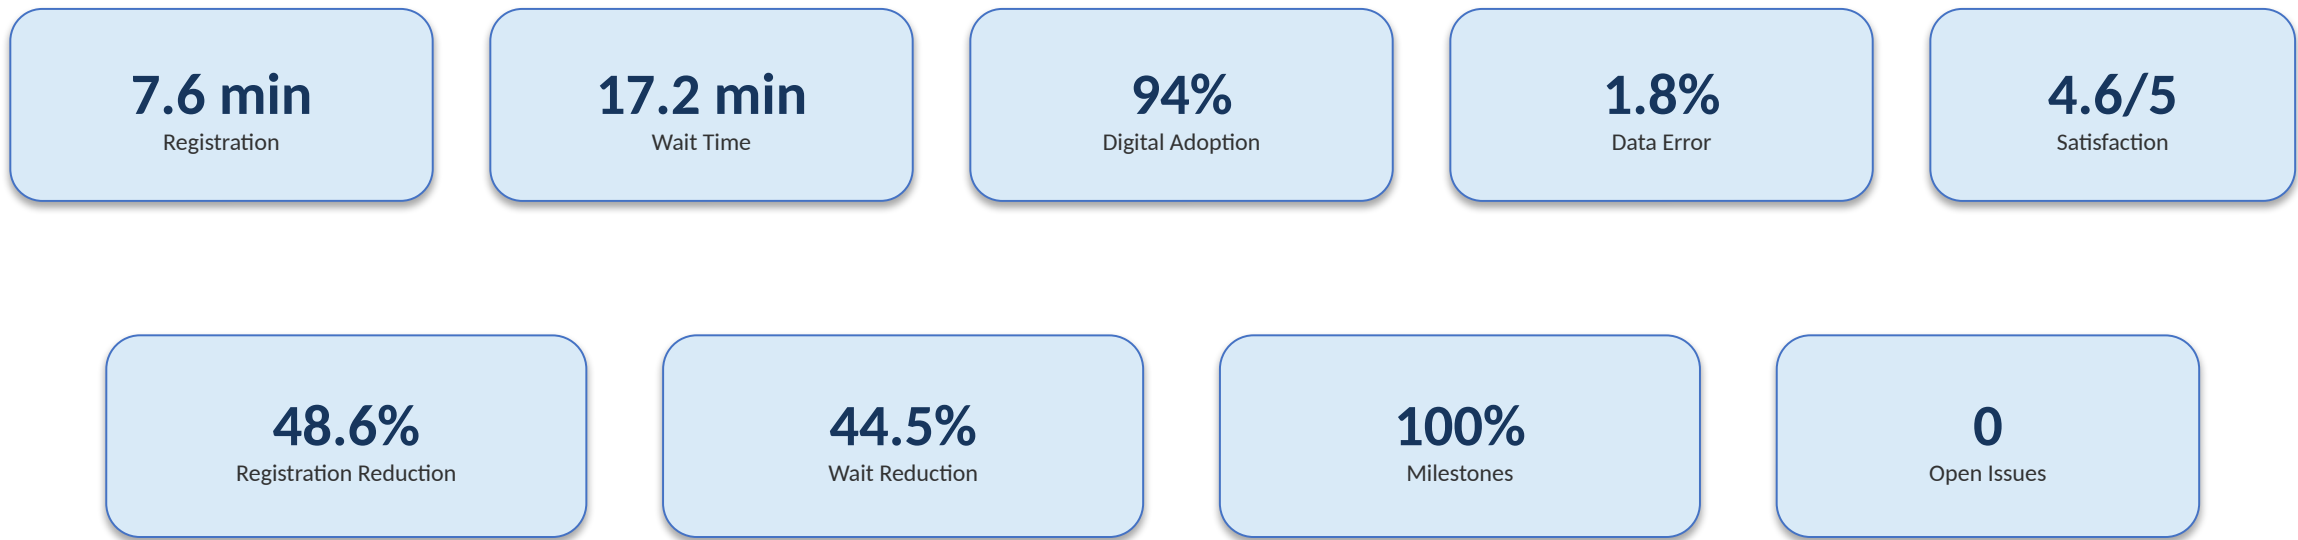

As-Is vs. To-Be Workflow

Paper / duplicate forms

AS-IS

Insurance verification after arrival

AS-IS

Repeated demographic entry

AS-IS

Late missing-field discovery

AS-IS

Inconsistent clinical handoff

AS-IS

Digital pre-registration

TO-BE

Pre-arrival eligibility queue

TO-BE

Verified demographic prepopulation

TO-BE


Real-time validation

TO-BE

Standard readiness checklist

TO-BE


Registration & Wait-Time Improvement

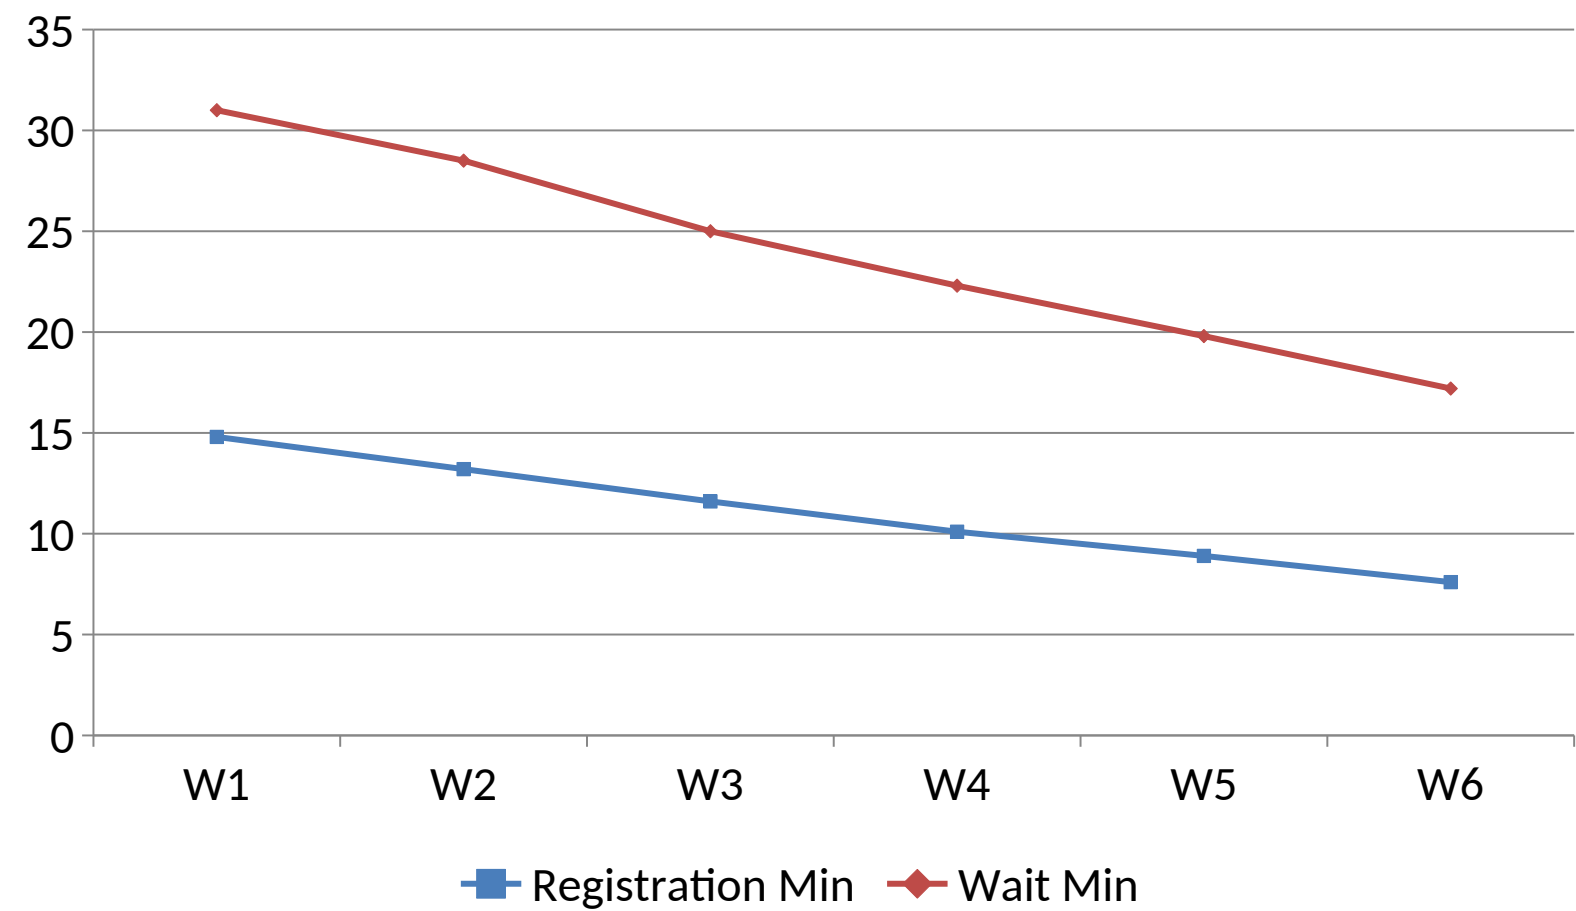

-48.6%
Registration

-44.5%
Wait Time

Adoption, Quality & Experience

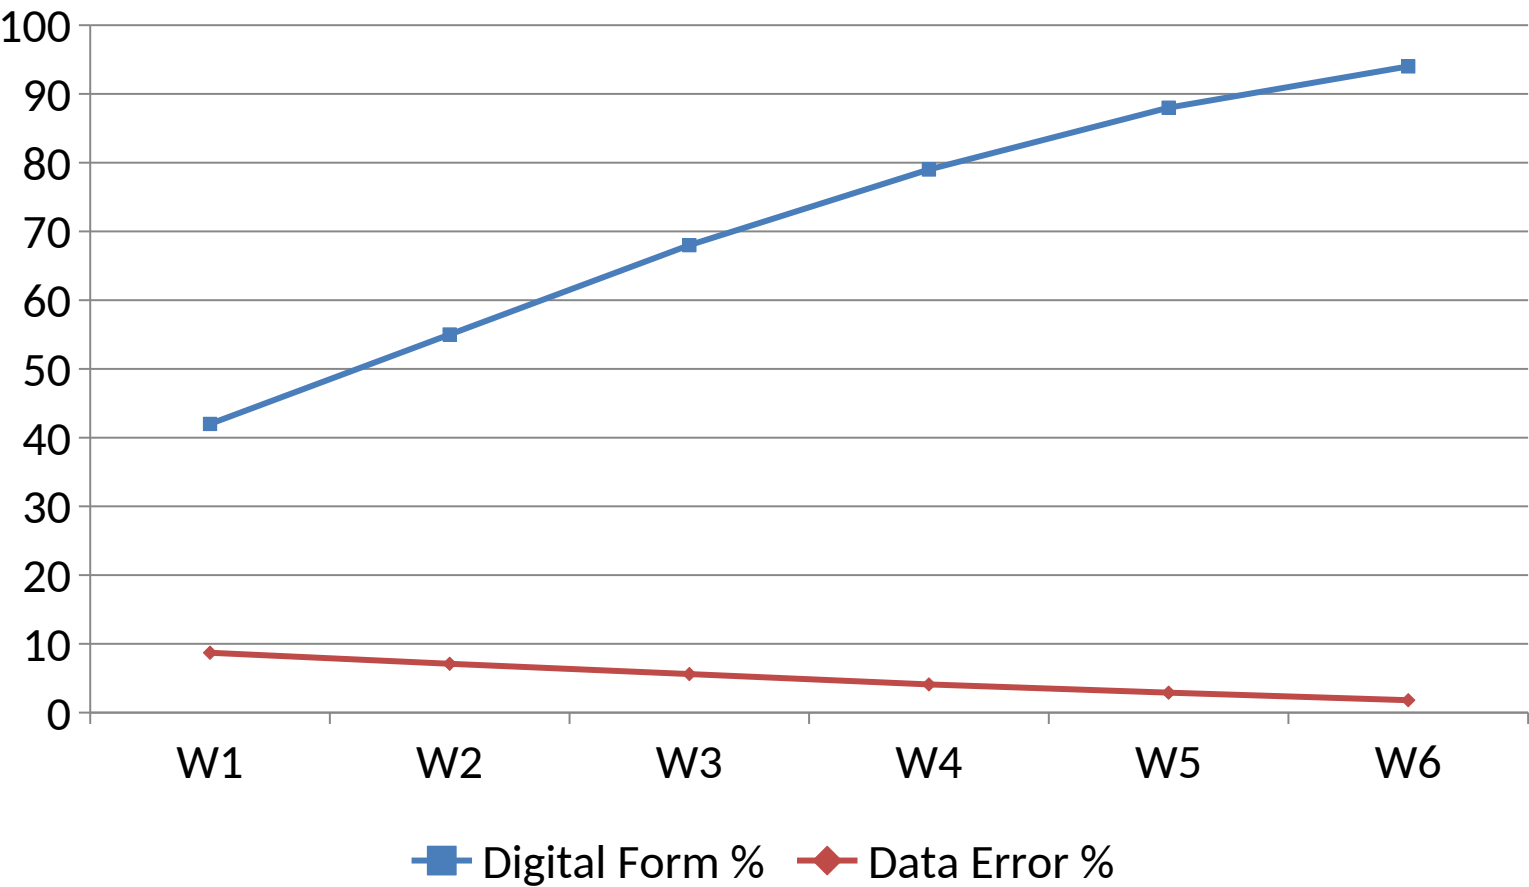

94%
Digital Adoption

1.8%
Data Error

4.6 / 5
Satisfaction

Milestone Performance

Charter Approved

On time

As-Is Mapping

On time

To-Be Design

1 day late

Pilot Ready

1 day early

Pilot Exit

On time

Full Rollout

On time

Closeout


On time

100%
Milestones

RAID & Defect Management

Duplicate guarantor mapping defect	I-01 Score 20 Closed
Clinical leadership approval	D-01 Score 20 Complete
Eligibility backlog risk	R-02 Score 15 Closed
Emergency digital adoption risk	R-01 Score 12 Closed
Department practice variation risk	R-03 Score 12 Closed

Budget Performance

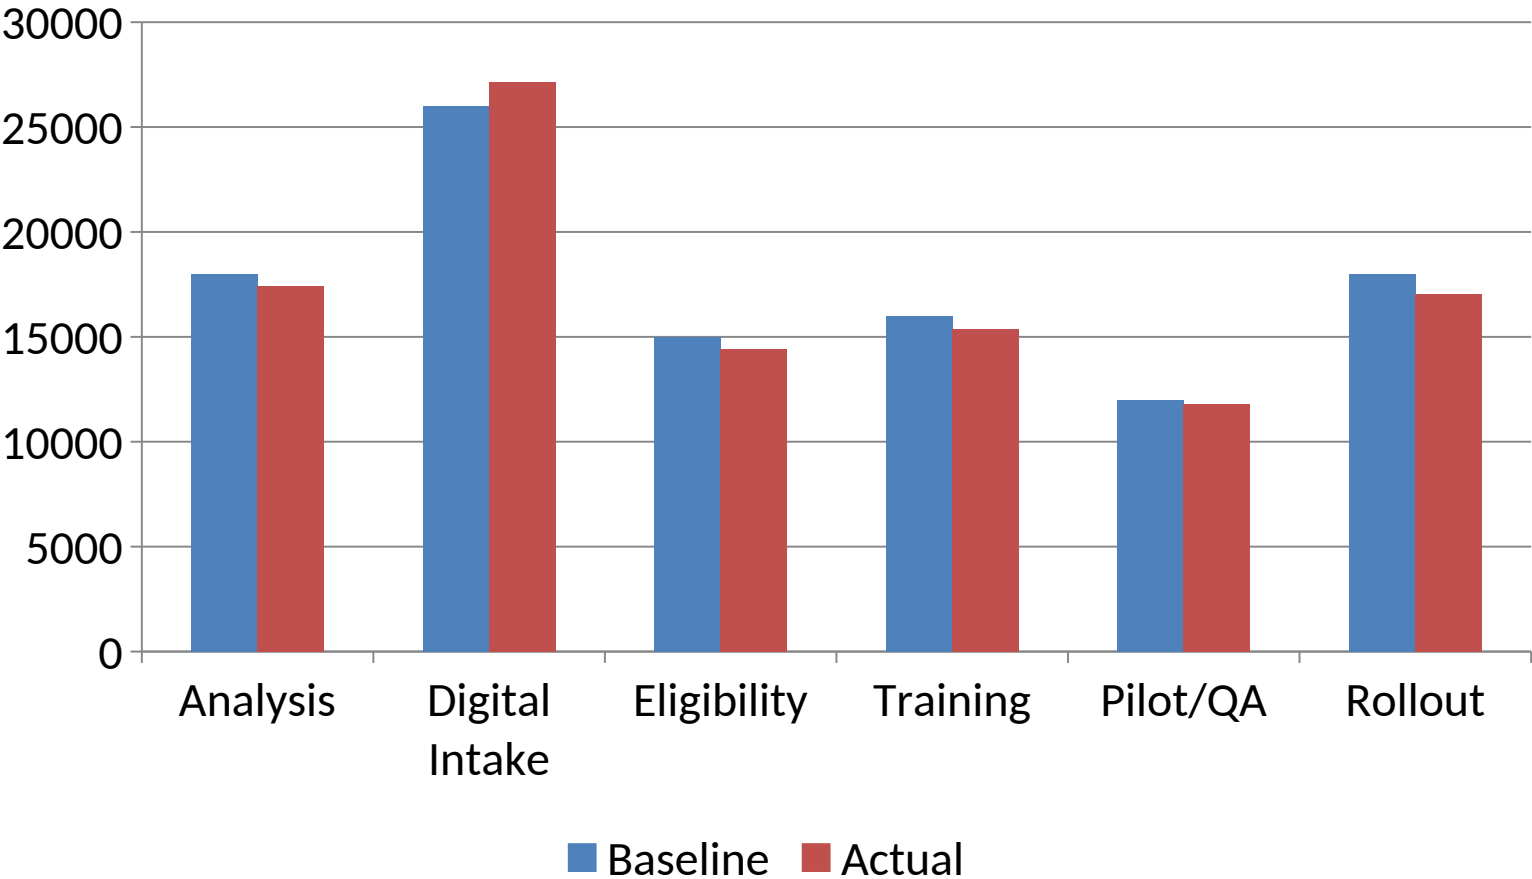

\$105K
Baseline

\$103.15K
Actual

\$1.85K
Favorable

Change Control & Lessons Learned

Approved Changes


Assisted digital intake station in Emergency Intake
Guarantor-field validation rule
Two-day pilot observation extension

Lessons Learned

Define eligibility queue ownership before shifting work upstream
Use real-time validation to prevent downstream rework
Pair defect severity with operational adoption in pilot exit criteria
Provide department-specific adoption support where needed

Closeout Summary

Simulated project objectives were met



Project Coordinator contribution

Coordinated process mapping, pilot, rollout, stakeholders, RAID, and changes.
Built formula-driven Excel operational reporting and executive visibility.
Tracked workflow efficiency, adoption, quality, satisfaction, milestones, and budget through closeout.
