

E-Commerce Platform Launch

Executive Project Update | Portfolio Case Study

Launch delivered on baseline date with favorable budget variance and zero open launch blockers.

Project Coordinator | Cross-functional delivery | 6-week simulated launch

Executive Health Dashboard

Week 6 - Launch & Hypercare

OVERALL

GREEN

Launch on plan

TASKS

100%

24 / 24 final week

VELOCITY

48

Up 100% vs Week 1

BUDGET

+1.7%

Favorable variance

BLOCKERS

0


At go-live

- Production launch completed August 17 as baselined.
- All critical launch-readiness criteria were satisfied before deployment.
- Hypercare monitoring active with no severity-1 incidents.


Scope & Delivery Model

- In scope: storefront, catalog, payment integration, UAT, security review, deployment, support readiness, hypercare.
- Out of scope: native mobile app, international expansion, second processor at initial launch, long-term optimization.
- Delivery gates: Initiate -> Plan -> Build & Configure -> Validate -> Launch -> Hypercare & Close.

E-Commerce Platform Launch - Delivery Workflow




Milestone Performance

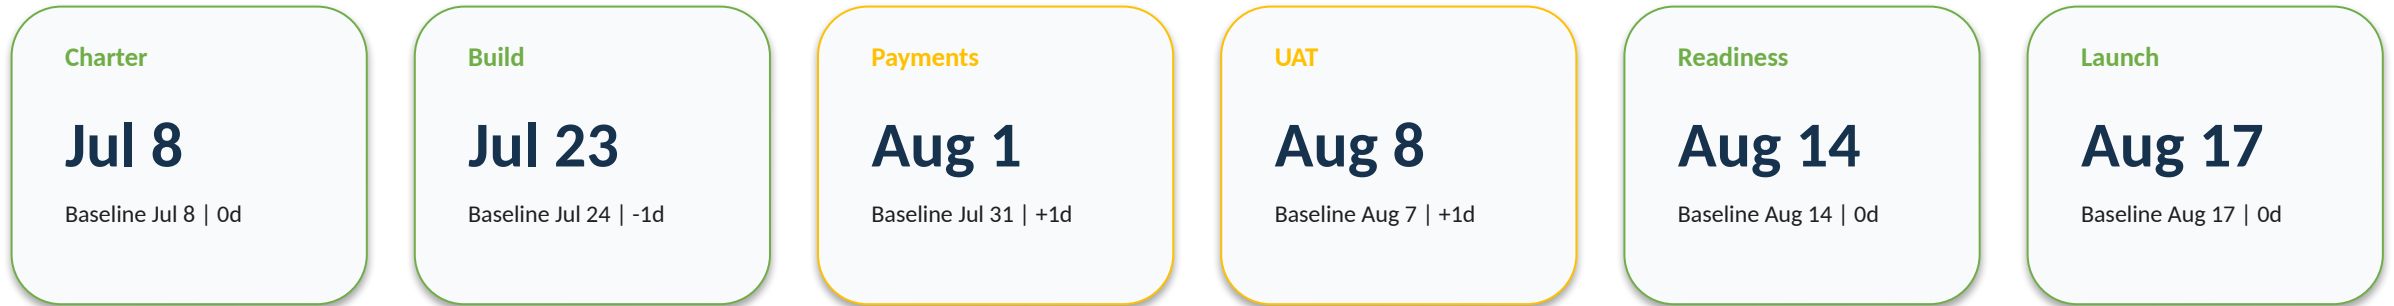

Schedule interpretation

- Two interim milestones moved by one day, but available float protected the August 17 launch baseline.
- No approved change request required a launch-date rebaseline.

Delivery Performance Trend

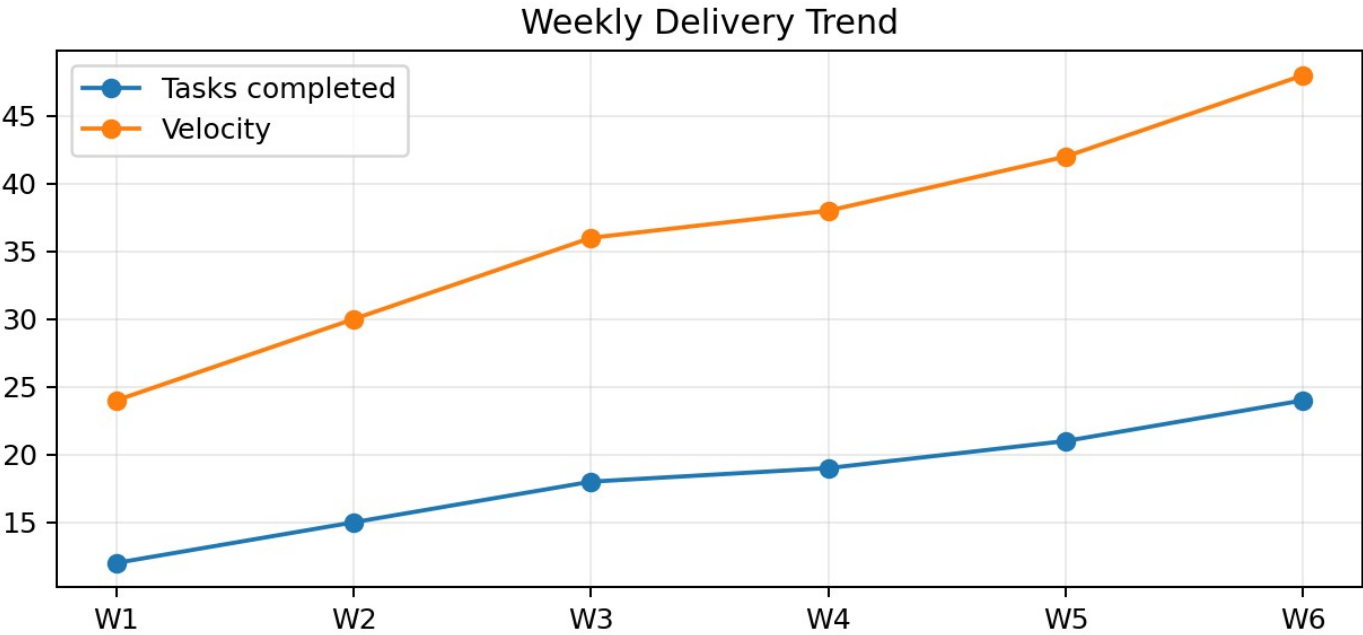

- Task throughput doubled from 12 to 24 completed tasks per week.
- Velocity increased from 24 to 48 across the six-week delivery period.
- Final week achieved 100% of planned tasks.

Top Risks, Issues & Dependencies

I-01

20

Issue score

Checkout defects during UAT

Mitigation tracked to named owner and target date.

CLOSED

D-01

20

Dependency score

Security approval before deployment

Mitigation tracked to named owner and target date.

COMPLETE

R-01

15

Risk score

Payment certification delay

Mitigation tracked to named owner and target date.

CLOSED

R-02

12

Risk score

Catalog data quality

Mitigation tracked to named owner and target date.

CLOSED

Budget & Forecast

BASELINE

\$90,000

Excludes \$5,000 contingency

ACTUAL

\$88,450

Completed below baseline

VARIANCE

+\$1,550

1.7% favorable

- Payment integration exceeded category baseline by \$800 due to certification support.
- Savings in platform development, QA, and hypercare offset the overage.
- Contingency remained available at project close.

Change Control & Decisions

- CR-01 Guest checkout - Approved. Three development days absorbed within schedule float.
- CR-02 Second payment processor - Deferred. Estimated two-week impact conflicted with launch baseline.
- CR-03 Additional 500 SKUs - Approved as phased upload with enhanced validation controls.
- Decision discipline protected the baseline while preserving business value in the post-launch backlog.

Go-Live Readiness

CRITICAL DEFECTS

0 open

Readiness criterion

SECURITY APPROVAL

Complete

Readiness criterion

PAYMENT VALIDATION

Passed

Readiness criterion

SUPPORT RUNBOOK

Accepted

Readiness criterion

ROLLBACK PLAN

Validated

Readiness criterion

MONITORING

Active

Readiness criterion

Outcome & Lessons Learned

- Launch completed on August 17 without rebaselining the target date.
- Final-week delivery reached 24/24 planned tasks; velocity increased 100% from Week 1.
- No launch-blocking issues remained open at go-live; spend finished 1.7% below baseline.
- Early dependency booking, daily UAT triage, and integrated tracking were the strongest execution controls.
- Portfolio note: this is a simulated case study created to demonstrate practical project coordination capability.
